Number	Cost	Priority	Projects	Description
1		4	Head Gate	Yearly maintenance
.			.	
2a		2	Long pipe (800lf)	NCRS?
.				
2b		1	Corner after long pipe	Build up embankment
.			.	
3		??	First trail crossing (town of New Castle)	Scope to be identified; schedule TBD
.			.	
4		1?	36" culvert, redslide pipe	3 man holes with grates
.			.	
5		2	Upstream of Rippy Pipe	No access; rockslide potential
.			.	
6		??	Rippy pipe	Straight pipe 36"
.			.	
7		1	Crooked pipe	220lf; 36" pipe: replace pipe (access difficult)
.			.	
8		1	Talbot pipe	100lf; in works with NRCS
.			.	
9		??	Trailer tressle pipe	? Scope
.			.	
10		2	Ditch bank problem	Suggest culvert 100' long
.			.	
11		??	Second trail crossing	Scope to be identified; schedule TBD
.			.	
12		3	Rummery culvert	May not be problem
.			.	
13		2	Joann Bauden open ditch	Determine if problem and suggest remedy
.			.	
14		??	Slaughter Gulch projects	Projects to be identified by sections 5+6

NOTES:

TO DO LIST

A. UNDERSTAND WATER CAPACITY ON PIPE SIZE + SLOPE; HOW MANY CFS

B. WHAT IS BASE COST? 36" DIAMETER=$100/LF; 48" DIAMETER=$150/LF, VERIFY LABOR@ $150 - $250/LF

C. LOOK INTO DRONE VIDEO

D. PREPARE PLAN FOR ALL #1 PRIORITY PROJECTS

E. OBTAIN INPUT FROM NCRS & POSSIBLE OTHER SOURCES

F. WORK ON MASTER PLAN FOR DITCH DOWNSTREAM OF SLAUGHTER GULCH; PIPE SIZING INFORMATION TBD

G. CONCLUDE NEGOTIATION WITH TOWN OF NEW CASTLE ON TRAIL CROSSINGS

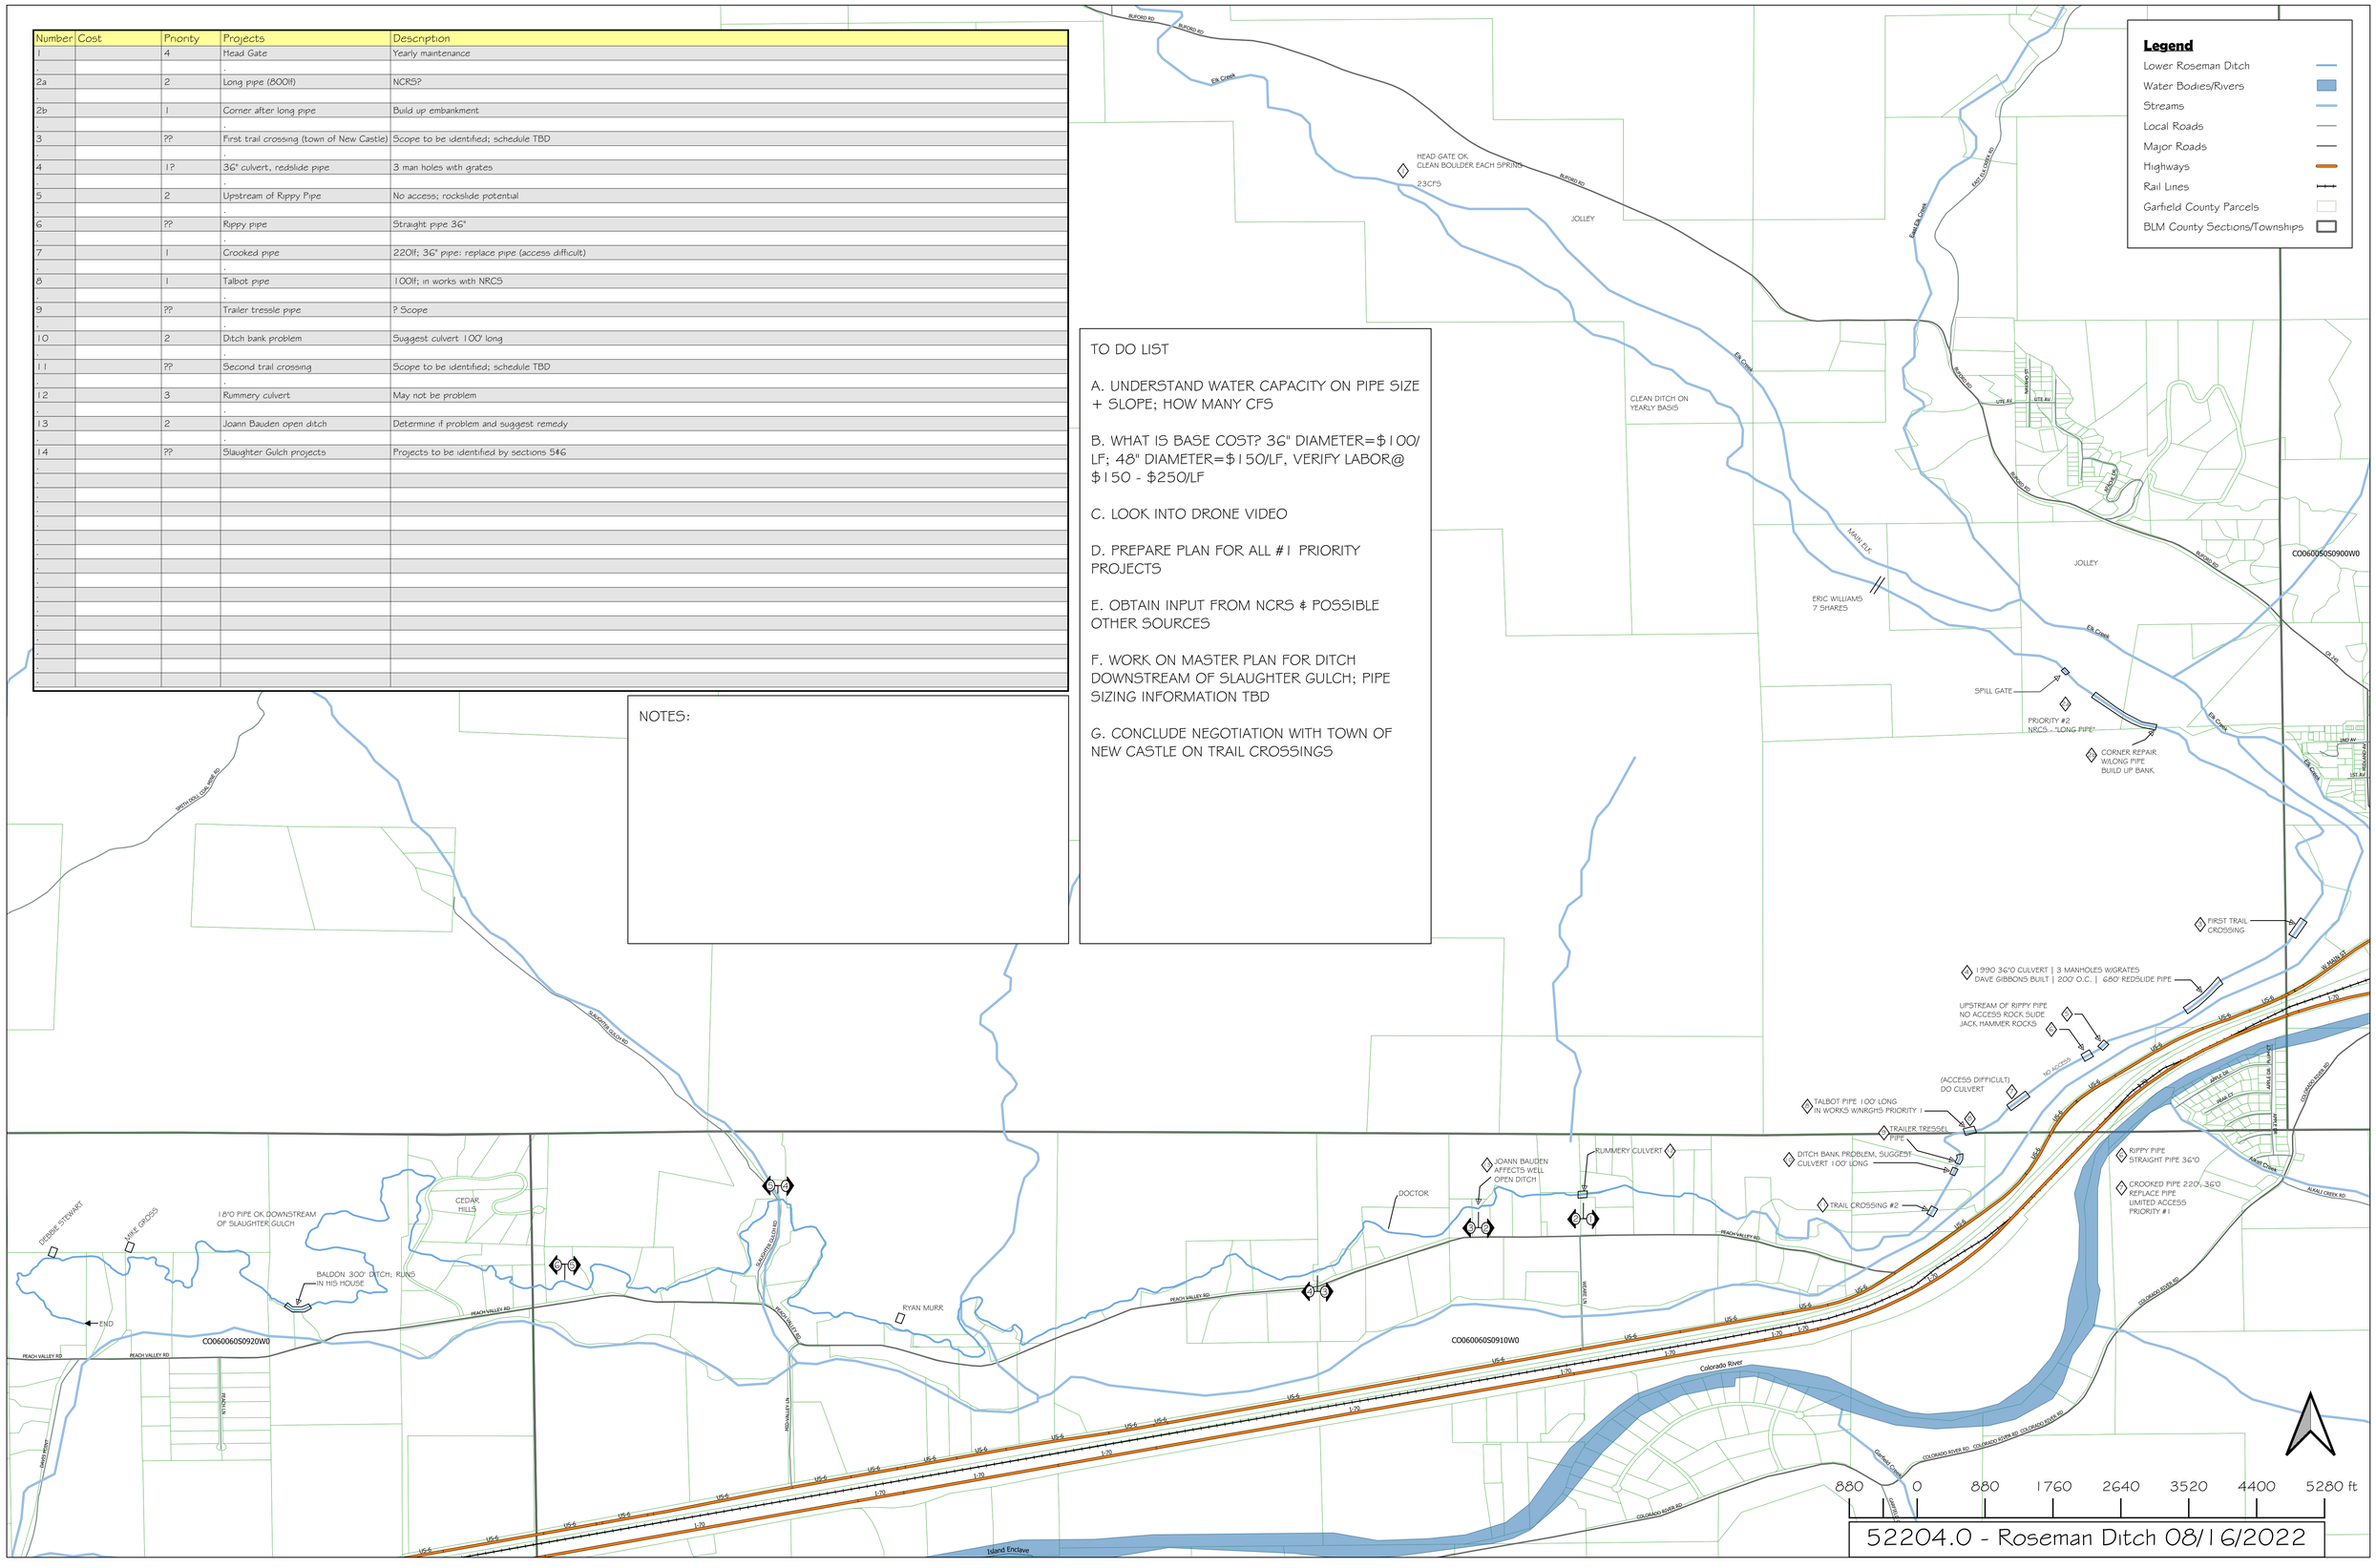

52204.0 - Roseman Ditch 08/16/2022
